QuickBite Agile Scrum Documentation

Part A: Scrum Team Organization

Member	Scrum Role	Responsibilities
Ricardo Morales Lopez	Product Owner / Developer	Database setup
Matthew Halliburton	Scrum Master / Developer	Search function
Cyril Szekiel Costes	Developer	Category grouping function
Michael Girgis	Developer	Testing, code review, and setup documentation

Part B: Definition of Done

Item	Criteria
1. Code Complete	Code complies with standard conventions.
2. Peer Reviewed	PR approved by at least one other developer.
3. Testing	Integration tests written and passed.
4. Acceptance Criteria	Verified by Product Owner against acceptance criteria.
5. Integration	Merged into the main branch without build errors.

Part B: Product Backlog

ID	Title	User Story	Acceptance Criteria	Priority	Estimate
PBI-01	Restaurant Browsing	As a Customer, I want to view and search restaurants by keyword or category so I can find where to order.	1. Displays restaurant card grid. 2. Search bar filters by name. 3. Filter buttons by category.	1	3 SP
PBI-02	Menu Viewing	As a Customer, I want to view a restaurant menu so I can select items.	1. Grouped by category. 2. Displays name and price.	2	3 SP

PBI-03	Cart Selection	As a Customer, I want to modify my cart so I can prepare an order.	1. Calculates total price. 2. Local storage persistence.	3	5 SP
PBI-04	Pickup Time Selection	As a Customer, I want to select a pickup time so my food is fresh.	1. 15-minute time slots. 2. Block past times.	4	3 SP
PBI-05	Order Placement	As a Customer, I want to submit an order with my contact info.	1. Capture name and phone. 2. Generate Order ID.	5	5 SP
PBI-06	Order Tracking	As a Customer, I want to view order status updates.	1. Display current status badge.	6	5 SP
PBI-07	Restaurant Dashboard	As a Restaurant Employee, I want to view incoming orders.	1. List orders chronologically.	7	5 SP
PBI-08	Status Control	As a Restaurant Employee, I want to update order status.	1. Support state transitions.	8	3 SP
PBI-09	Database Setup	Set up database models and seed data.	1. Seed script populates restaurants.	9	2 SP
PBI-10	Error Boundary	Handle API failures gracefully.	1. Toast error on 500 status.	10	2 SP

Fi

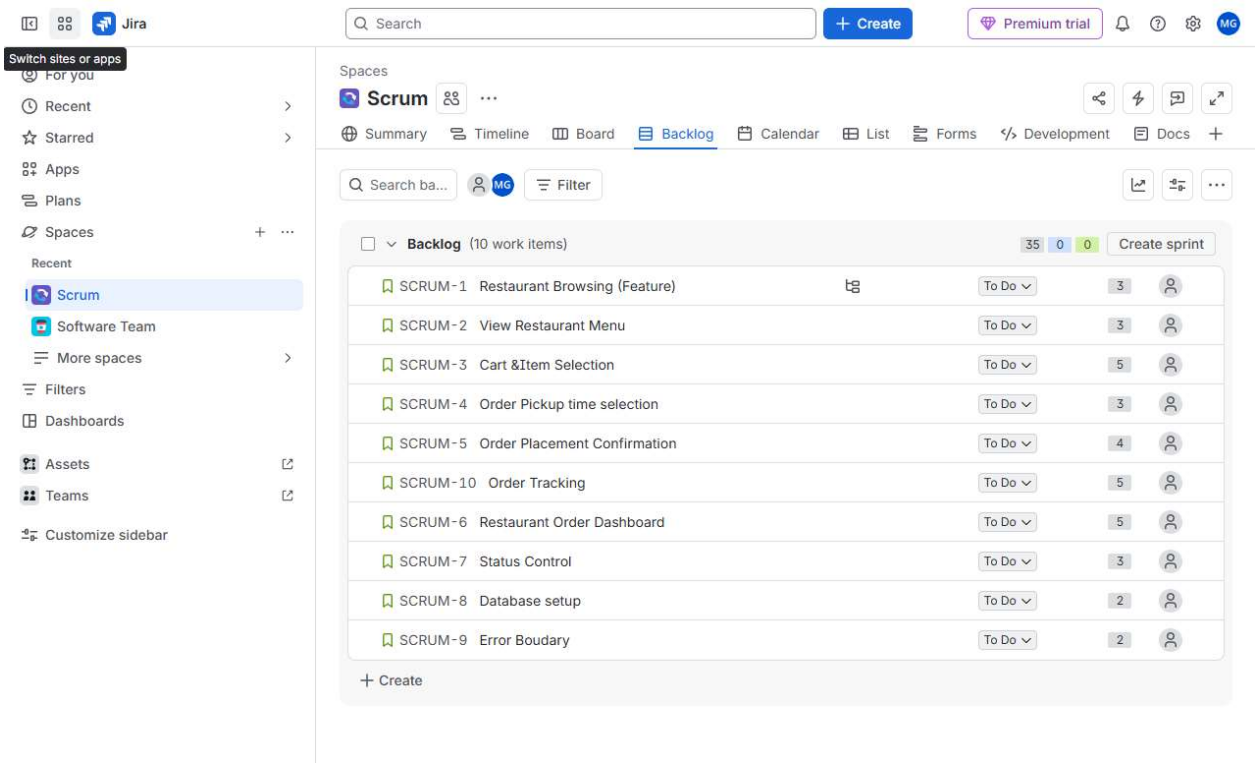


Figure 1. Product Backlog.

Part B: Product Owner Priority Rationale

Rank	PBI	Rationale
1	PBI-01: Restaurant Browsing	Core focus for Sprint 1. Delivers restaurant list, search, and category filter value immediately.
2	PBI-02: Menu Viewing	Direct next dependency for customer interaction.
3	PBI-03: Cart Selection	Connects menu selection to order checkout.
4	PBI-04: Pickup Time Selection	Required for scheduled pickup functionality.
5	PBI-05: Order Placement	Completes the transaction flow.

Part C: Sprint Planning

Parameter	**Details**
Sprint Goal	Allow a customer to browse, search, and category-filter participating restaurants on the QuickBite platform.
Capacity	4 members x 2 hours/week = 8 hours.
Selected Scope	PBI-01: Restaurant Browsing (3 Story Points).

Part C: Engineering Tasks

PBI	**Task Description**	**Assigned**	**Hours**
PBI-01	TASK-101: Design database for restaurants & categories	Ricardo	1h
PBI-01	TASK-102: Implement Search method that takes the user input as params	Ricardo	1h
PBI-01	TASK-103: Create keyword search bar component	Matthew	1h
PBI-01	TASK-104: Connect search component to database	Matthew	1h
PBI-01	TASK-105: Build category grouping & filter buttons	Cyril	1h
PBI-01	TASK-106: Integrate category filter with main restaurant grid list	Cyril	1h
PBI-01	TASK-107: Write Integration tests for search & category filtering	Michael	1h
PBI-01	TASK-108: Conduct peer code review	Michael	1h

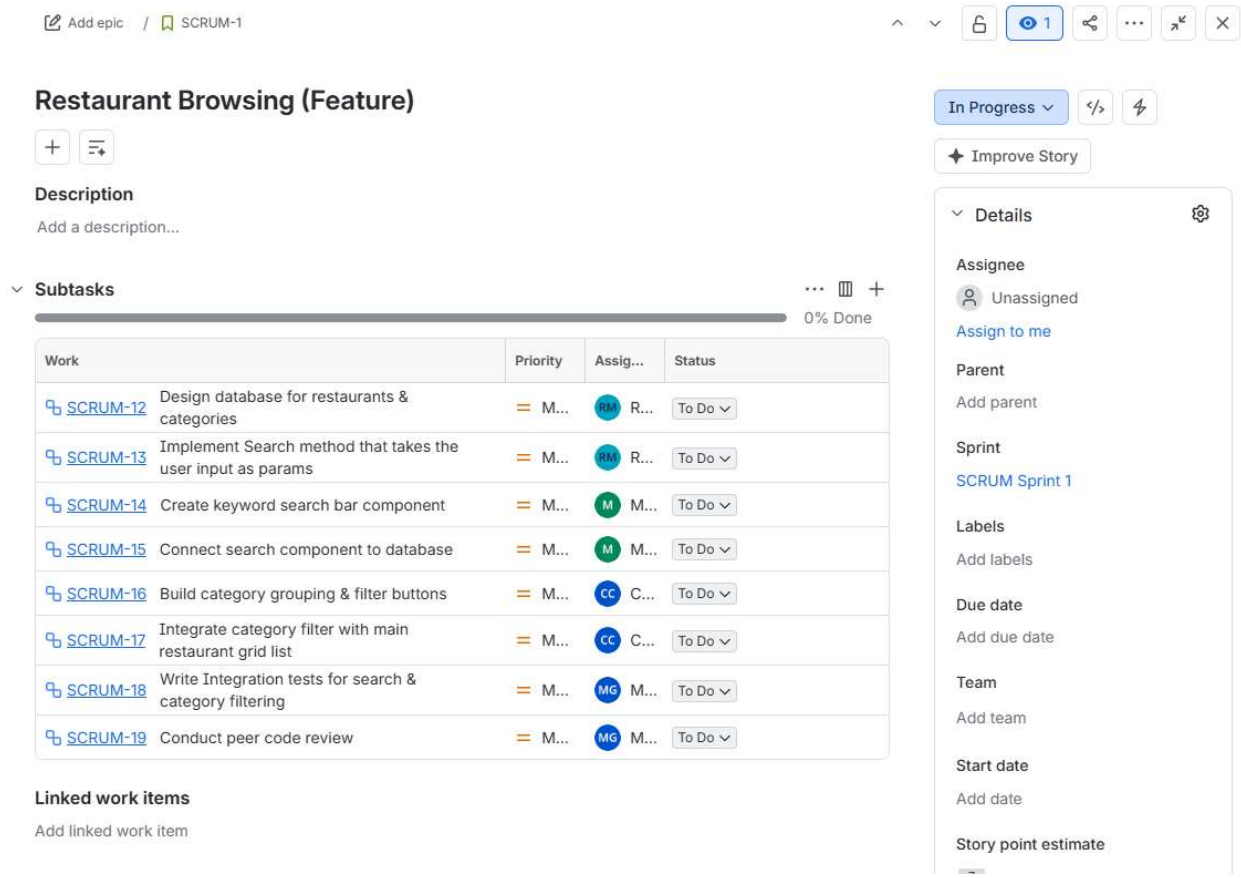


Figure 2. Sprint Backlog.

Part D: Git Commit Log

Hash	Author	Branch	Commit Message
	Ricardo Morales Lopez	main (PR #4)	Merge PR #4: Database setup and search method.
	Matthew Halliburton	feature/restaurant-search	FEAT: Implement keyword search function component
	Cyril Szekiel Costes	feature/category-filter	FEAT: Implement category grouping filter component

Part D: Working Increment Execution

Step	Role	System Flow
1	Customer	Navigates to the QuickBite home page.
2	Customer	Views restaurant list seeded from database set up by Ricardo.
3	Customer	Types 'Taco' into search bar built by Matthew and new grid with this keyword shows up
4	Customer	Clicks 'Mexican' category tag built by Cyril and the grid filters by category.

Part E: Daily Scrums

Event	Progress	Impediments	Decisions / Adaptations
Daily Scrum 1 (Day 1)	Ricardo set up database and Matthew built search bar UI draft.	Uncertainty on whether category filtering should be client-side or backend-driven.	Agreed Ricardo provides category fields in the database so that the backend handles the filtering dynamically.
Daily Scrum 2 (Day 2)	Search bar connected to the database and Cyril drafted category grouping component.	Cyril is blocked on standardizing category names across backend and frontend.	Ricardo updated the database file with standard category strings (e.g., 'Italian', 'Mexican').
Daily Scrum 3 (Day 3)	Search and category functions fully integrated and Michael completed test execution.	Received mid-sprint change request regarding distance to restaurant based sorting.	Decided to maintain current Sprint Goal; added distance request to Sprint 2 backlog.

Part F: Mid-Sprint Change Analysis

Dimension	Analysis
Request	Restaurants want search results to filter by active workload status and max distance.
Change	Shift from basic keyword search & category grouping to distance/workload filtering.
Questions	1. Should distance be calculated via GPS or postal code? 2. What defines workload status?
New PBIs	PBI-11: Distance/Workload Search Filters (3 SP)
Sprint Impact	None. Active Sprint Goal remains focused solely on basic browsing, search, and categories.
Action	Added PBI-11 to Product Backlog for evaluation in Sprint 2.

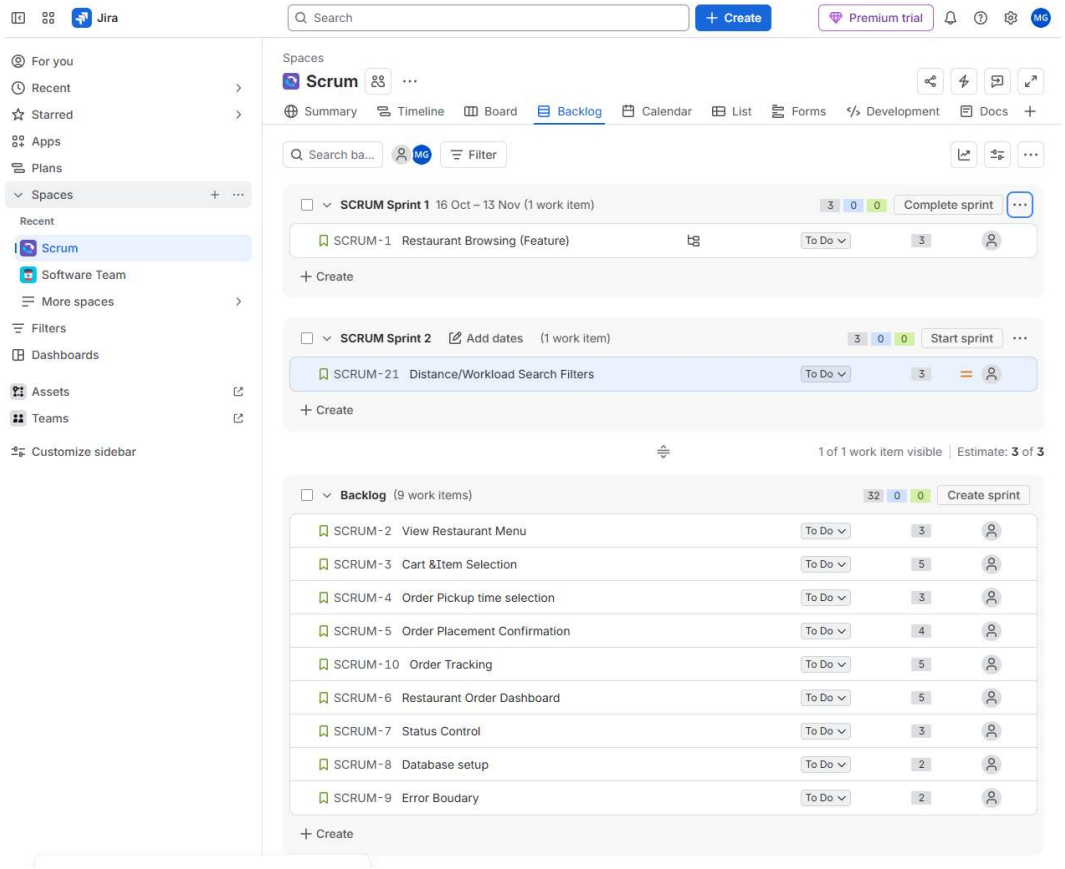


Figure 3. Sprint 2 planned to be for Distance/Workload filter.

Part G: Sprint Review Feedback

#	Feedback	Decision	Backlog Action
1	Add multi-category selection so users can select 'Mexican' AND 'Fast Food'.	Accept	Added PBI-12: Multi-Category Filter Support.
2	Show estimated delivery time on the restaurant card.	Reject	Deferred. QuickBite is pickup-only.
3	Highlight open vs closed status with clearer badge colors.	Accept	Updated PBI-01 acceptance criteria.

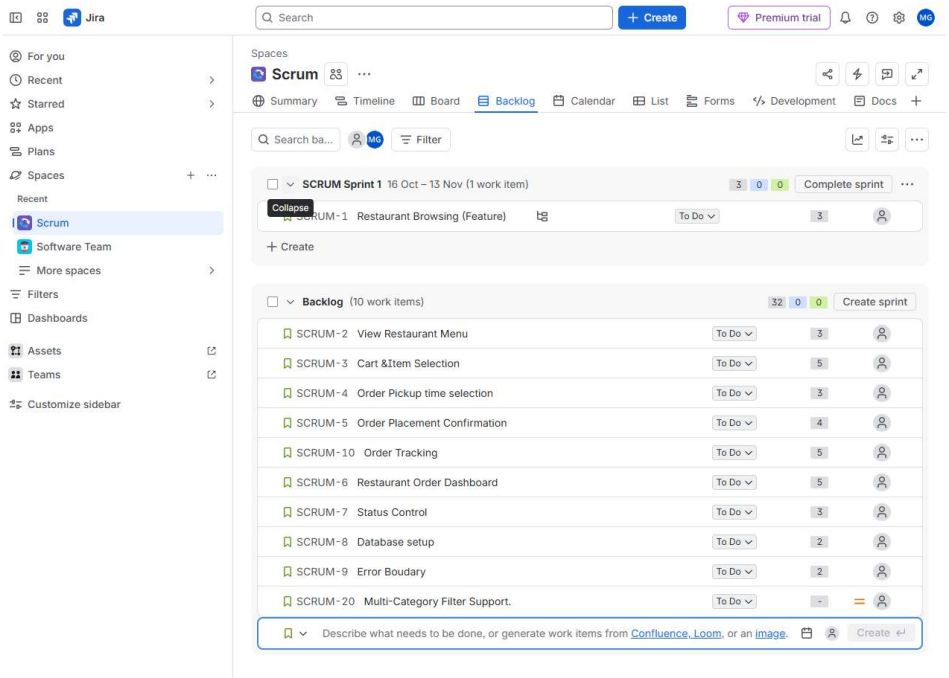


Figure 4. The backlog with the added PBI-012, Multi-Category Filter Support.

Part H: Sprint Retrospective

Topic	Findings
What went well	Aligning member tasks strictly to Database (Ricardo), Search (Matthew), and Categories (Cyril) enabled parallel development.
What did not go well	Minor alignment delays on standardizing category name strings between database and client side.
What slowed us down	Waiting on database seed structure before client side category buttons could be tested.
What helped	Using simple mock test file category responses early.

DoD effectiveness	Effective. Peer code reviews by Michael caught search input edge cases.

Part H: Improvement Action Items

#	**Type**	**Action Item**	**Implementation**
1	Process	Define app mocks first	Commit static mock test files before writing endpoint logic.
2	Technical	Debug client side before PR	More commits to debugging before PR creation.

Agile Analysis:

We demonstrated agility effectively in this small working increment. We delivered small pieces of code each in order to get one work product demonstrating incremental delivery. We also got a sudden change from the product owner mid-project in which they wanted to add a new feature to the app to filter results based on distance and we responded to that change by moving it into the next scrum task showing that we will implement it in the next iteration. The stakeholders provided feedback on our first work product demonstrating stakeholder collaboration. We took the feedback from stakeholders and altered the work product to fit that feedback. We also observed improvements amongst ourselves which we will keep in mind for the next sprint showing continuous improvement with each iteration.

GenAI Disclosure: We used Gemini to help brainstorm ideas and suggest a possible scenario for this QuickBites software. We analyzed its response and developed our response to reflect this brainstorming as well as implement our ideas for Part A - Part H.
